Public Disclosure Authorized
Public Disclosure Copy

Implementation Status & Results
Russian Federation
Registration Project (P093050)

Operation Name: Registration Project (P093050) | Project Stage: Implementation | Seq.No: 13 | Status: ARCHIVED | Archive Date: 24-Jun-2013

Country: Russian Federation | Approval FY: 2006

Product Line: IBRD/IDA | Region: EUROPE AND CENTRAL ASIA | Lending Instrument: Specific Investment Loan

Implementing Agency(ies): FER

Key Dates

Board Approval Date	13-Jun-2006	Original Closing Date	31-May-2014	Planned Mid Term Review Date		Last Archived ISR Date	26-Dec-2012
Effectiveness Date	23-Apr-2008	Revised Closing Date	31-May-2014	Actual Mid Term Review Date			

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The new Project Development Objective is to improve the system of registration of legal rights to immovable property by developing standardized, clear and more efficient registration procedures, and by introducing an improved information management system for the registration offices.

Has the Project Development Objective been changed since Board Approval of the Project?

◉ Yes ○ No

Component(s)

Component Name	Component Cost
Institutional Development of the Registration Service	17.80
Information and Communications Systems	27.40
Improvement of professional skills of registration staff	1.20
Project Management	3.60

Overall Ratings

	Previous Rating	Current Rating
Progress towards achievement of PDO	Moderately Unsatisfactory	Moderately Unsatisfactory
Overall Implementation Progress (IP)	Moderately Unsatisfactory	Moderately Unsatisfactory
Overall Risk Rating	Moderate	Moderate

Implementation Status Overview

The project continues to move steadily toward meeting the Project Developments Objective (PDO) of an improved registration system, providing key inputs for the institutional and technological development of Rosreestr. Most areas of the project are on track to achieve their objectives and Rosreestr continues to improve its overall operating environment and strategy in notable ways. Disbursement of the loan, however, continues to lag behind the planned schedule.

Public Disclosure Copy

Locations

Country	First Administrative Division	Location	Planned	Actual
Russian Fed.	Not Entered	Yaroslavskaya Oblastí		
Russian Fed.	Not Entered	Voronezhskaya Oblastí		
Russian Fed.	Not Entered	Volgogradskaya Oblastí		
Russian Fed.	Not Entered	Ulíyanovskaya Oblastí		
Russian Fed.	Not Entered	Udmurtskaya Respublika		
Russian Fed.	Not Entered	Tverskaya Oblastí		
Russian Fed.	Not Entered	Tul'skaya Oblast'		
Russian Fed.	Not Entered	Respublika Tatarstan		
Russian Fed.	Not Entered	Stavropolískiy Kray		
Russian Fed.	Not Entered	Saratovskaya Oblast'		
Russian Fed.	Not Entered	Samarskaya Oblastí		
Russian Fed.	Not Entered	Rostovskaya Oblastí		
Russian Fed.	Not Entered	Perm Krai		
Russian Fed.	Not Entered	Novgorodskaya Oblastí		
Russian Fed.	Not Entered	Murmanskaya Oblastí		
Russian Fed.	Moscow	Moskva		✓
Russian Fed.	Not Entered	Moscow		
Russian Fed.	Not Entered	Lipetskaya Oblastí		
Russian Fed.	Not Entered	Sankt-Peterburg		
Russian Fed.	Not Entered	Kurskaya Oblastí		
Russian Fed.	Not Entered	Krasnodarskiy Kray		
Russian Fed.	Not Entered	Kirovskaya Oblastí		
Russian Fed.	Not Entered	Kaluzhskaya Oblastí		
Russian Fed.	Not Entered	Kaliningradskaya Oblastí		

Public Disclosure Copy

Public Disclosure Copy

Country	First Administrative Division	Location	Planned	Actual
Russian Fed.	Not Entered	Nizhegorodskaya Oblastí		
Russian Fed.	Not Entered	Chuvashskaya Respublika		
Russian Fed.	Not Entered	Bryanskaya Oblastí		
Russian Fed.	Not Entered	Belgorodskaya Oblastí		
Russian Fed.	Not Entered	Respublika Bashkortostan		
Russian Fed.	Not Entered	Arkhangelískaya Oblastí		
Russian Fed.	Not Entered	Vladimirskaya Oblastí		
Russian Fed.	Not Entered	Tyumenskaya Oblastí		
Russian Fed.	Not Entered	Sverdlovskaya Oblastí		
Russian Fed.	Not Entered	Novosibirskaya Oblastí		
Russian Fed.	Not Entered	Krasnoyarskiy Kray		
Russian Fed.	Not Entered	Kemerovskaya Oblastí		
Russian Fed.	Not Entered	Chelyabinskaya Oblastí		
Russian Fed.	Not Entered	Primorskiy Kray		
Russian Fed.	Not Entered	Khabarovskiy Kray		
Russian Fed.	Not Entered	Irkutskaya Oblastí		

Results

Project Development Objective Indicators

Public Disclosure Copy

Public Disclosure Copy

Public Disclosure Copy

Indicator Name	Core	Unit of Measure		Baseline	Current	End Target
Client Satisfaction	☐	Percentage	Value	60.00	72.00	78.00
			Date	30-Dec-2005	08-Jun-2013	31-May-2014
			Comments	Not available	With over 5000 offices and more than 40,000 employees, Rosreestr faces an enormous challenge to provide satisfactory, standardized client services across the country, and to integrate fully the different contituent agencies which were merged to form Rosreestr into a single management structure with unified performance standards and monitoring, homogeneous human resource management practices, and a unified corporate identity. However, there is progress in supporting these developments.	
Reduction in time for registration (first time, sales, inheritance, other)	☐	Days	Value	30.00	20.00	15.00
			Date	30-Dec-2005	08-Jun-2013	31-May-2014
			Comments		The unified IT system was officially launched on January 1, 2013. The work on the NSDI implementation is progressing well: NSDI WEB Portal has been opened, the new draft law on Geodesy, Cartography and SDI is ready for parliamentary procedure.	
Increased productivity of the unified registration staff	☐	Number	Value	700.00	743.00	1200.00
			Date	30-Dec-2005	08-Jun-2013	31-May-2014
			Comments	Number of transactions per staff/year.	Number of transactions per staff/year. Several activities for improvement of professional skills are in the process of	Number of transactions per staff/year.

Public Disclosure Copy

					contracting and/or implementation. No new measurement taken this year.	
Avg no. of days to complete recordn of purchase/sale of property in land adm systm	☒	Number	Value	30.00	20.00	15.00
			Date	30-Dec-2005	08-Jun-2013	31-May-2014
			Comments		The unified IT system was officially launched on January 1, 2013., No new measurement of indicator this year.	
Avg no. of days to complete recordn of purchase/sale of property–Urban	☒	Number Sub Type Breakdown	Value	0.00	0.00	0.00
			Date			
			Comments	Not available	Not available	Not available
Avg no. of days to complete recordn of purchase/sale of property–Rural	☒	Number Sub Type Breakdown	Value	0.00	0.00	0.00
			Date			
			Comments	Not available	Not available	Not available

Intermediate Results Indicators

Indicator Name	Core	Unit of Measure		Baseline	Current	End Target
Increase of archive capacity (files per m2)	☐	Text	Value	27 offices currently using scanned data.	27 offices currently using scanned data	To be determined in strategy and monitored.
			Date	30-Dec-2005	08-Jun-2013	31-May-2014
			Comments		It was requested to make additional amendments to the Archive Strategy. This has led to additional delay in the Archive Strategy completion and final approval.	
Increase in the percentage of surveyed population that understands the requirements and procedures for registration	☐	Text	Value	70%	84%	91%
			Date	30-Dec-2005	08-Jun-2013	31-May-2014
			Comments		No new measurement this year.	
Reduction in time for processing information requests from individuals	☐	Text	Value	7 days	1	Within 1 day
			Date	30-Dec-2005	08-Jun-2013	31-May-2014
			Comments		The target has been achieved for on-line requests for information and provision of electronically signed extracts. The number electronically	

Public Disclosure Copy

Public Disclosure Copy

					signed extracts have been increased more than twice during the last six months. Extracts can be obtained from any Rosreestr office or from Multifunctional centers for the entire territory of Russian Federation	
Technical capacity to receive and transmit information between Registration and other Federal Agencies, including Cadastre Offices	☐	Text	Value	0	100 percent	80 percent
			Date	30-Dec-2005	08-Jun-2013	31-May-2014
			Comments	Number/percent of offices using electronic query	The indicator has been achieved. Currently all 83 SRF (regions) have the necessary technical capacity and obliged to provide information to all Government, regional and municipal services.	All RF subjects of the Federation
Increase in information requests	☐	Text	Value	0	Increasing	To be monitored
			Date	30-Dec-2005	08-Jun-2013	31-May-2014
			Comments		The number of electronic requests - hits on databases- baseline 0 is continuous increasing.	
Number of RosReestr Staff trained using single window technology	☐	Number	Value	0.00	1100.00	640.00
			Date	31-Dec-2005	08-Jun-2013	31-May-2014
			Comments		Several activities for improvement of professional skills are in the process of contracting and/or implementation.	Move to on-line training system available for all Rosreestr staff. Target from original PAD.
Submission to Government a set of normative acts for improvements in the unified Registration System	☐	Text	Value		Phase 1 and 2 completed, Phase 3 not completed	Submitted.
			Date	31-Dec-2005	08-Jun-2013	31-May-2014
			Comments		The preparation of the necessary laws and series of regulations have been developed. It is in a final phase, which will be completed by August 2013.	

Public Disclosure Copy

Data on Financial Performance (as of 06-May-2013)

Public Disclosure Copy

Financial Agreement(s) Key Dates

Project	Ln/Cr/Tf	Status	Approval Date	Signing Date	Effectiveness Date	Original Closing Date	Revised Closing Date
P093050	IBRD-48260	Effective	13-Jun-2006	14-Sep-2007	23-Apr-2008	31-May-2014	31-May-2014

Disbursements (in Millions)

Project	Ln/Cr/Tf	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P093050	IBRD-48260	Effective	USD	50.00	50.00	0.00	8.65	41.36	17.00

Disbursement Graph

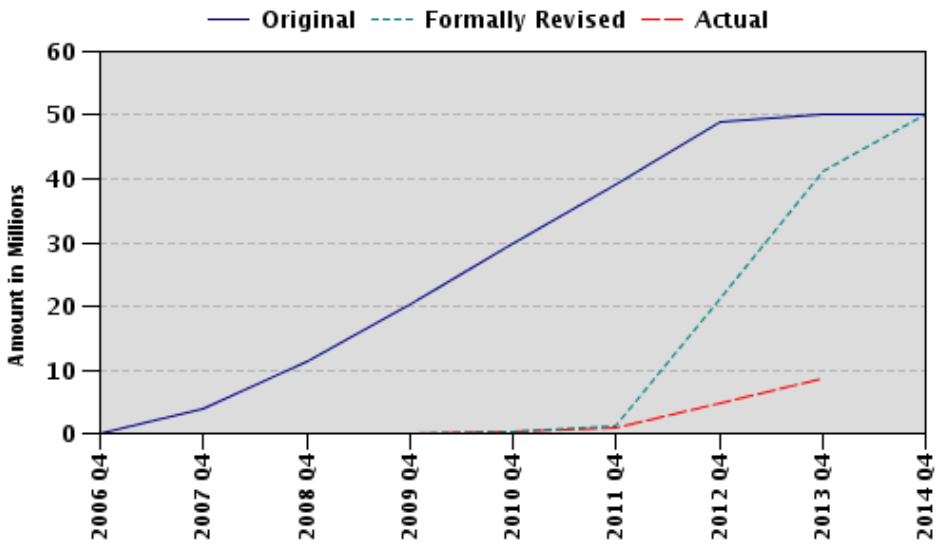

Key Decisions Regarding Implementation

None

Restructuring History

Level one Approved on 23-Aug-2010

Related Projects

There are no related projects.

Public Disclosure Copy
